



US-89

FARMINGTON TO I-84

Community Coordination Team Construction Phase Meeting #6

December 17, 2020

MEETING AGENDA

Welcome & Core Value Moment

2020 CCT Scores

Year in Review

Upcoming Construction Activities

CCT Member Questions/Feedback

Vote

PROJECT CORE VALUES

Core Values

Trust

Safety

Fiscal Responsibility

Passion

Public Responsiveness

Dedication



CCT SCORES TO DATE:

Areas of Evaluation	May	July	Sept.	Oct.	Avg.
Responsiveness	6.57	6.57	6.86	7	6.75
Transparency	6.625	6.83	6.86	6.86	6.79
Traffic control	6.75	6.5	6.71	7	6.74
Safety	6.625	6.33	6.86	7	6.7
Housekeeping/ Site cleanliness	6.125	6	6.43	6.57	6.28
Overall Score	6.539	6.446	6.74	6.89	6.654



CONSTRUCTION PROGRESS UPDATE

Project to Date

- Storm drain is **30%** complete
- Third-party utilities (gas, electric, cable, etc.) are **42%** complete
- Wet utilities (water lines, sewer, etc) are **40%** complete
- **500,000 cubic yards** of earth moved and placed
- **50,000 tons** of permanent asphalt placed
- **16,000** density tests taken
- **400** proctors (verify weight of material)
- **4,000** inspections
- Nearly **800,000** hours of work
- Girders set at Oak Hills and 200/400 North

CONSTRUCTION PROGRESS UPDATE

Utility Work Completed to Date

Weber Basin Culinary Water

Serves approximately 140,000 residents through Layton, Kaysville, and Fruit Heights.


Completed*:

- 2,400 LF of 36" Welded Steel Pipe
- 6,240 LF of 30" Welded Steel Pipe
- 2,000 LF of 24" Ductile Iron Pipe

Yet to be installed:

- 980 LF of 36" Welded Steel Pipe
- 2,600 LF of 24" Ductile Iron Pipe

* There will still be some shutdowns for permanent tie-ins

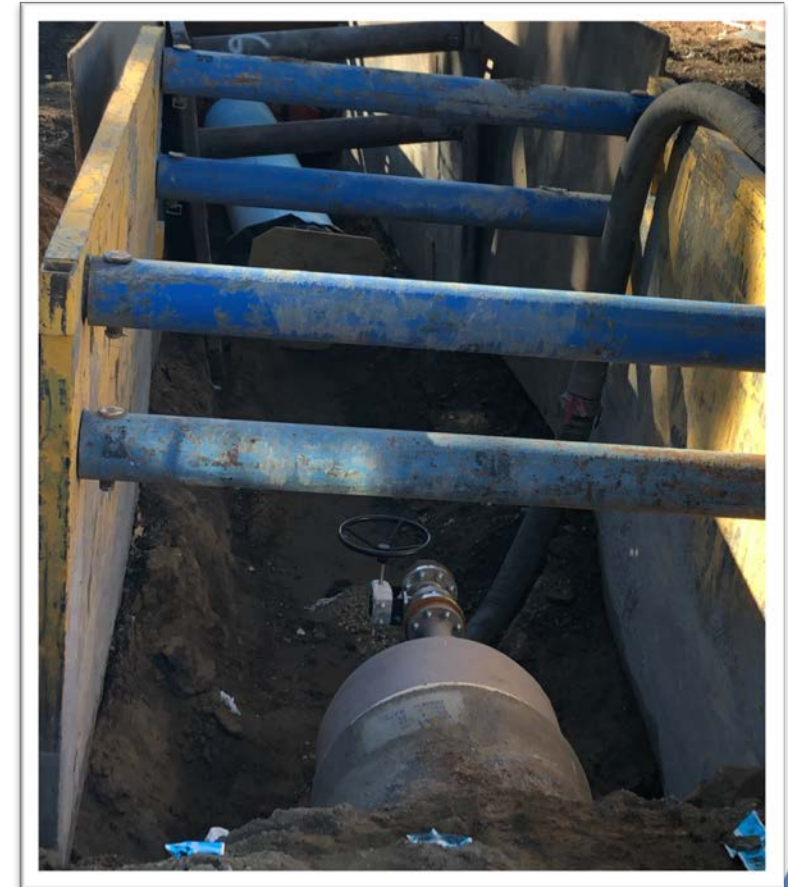

CONSTRUCTION PROGRESS UPDATE

Utility Work Completed to Date

City Water Lines

Layton

- 19,751 LF new water lines between 1400 N to Oak Hills Drive
- Connected to the new Layton water tank & removed old tank at Oak Hills Drive interchange
- 2,674 LF of sewer lines in the new Gordon Ave interchange for future development

Kaysville

- 11,763 LF of water lines
- 2,459 LF of Central Davis Sewer District lines
- 1,850 LF of Central Davis Canal Company irrigation lines
- In the new frontage roads to clear the area for the new Crestwood bridge construction in 2021.

Fruit Heights

- 3,610 LF relocated at the new 400 N intersection
- 3,111 LF of Haight's Creek Irrigation lines along Country Way.
- Water line relocation on the east side of 400 N intersection will take place in early 2021

CONSTRUCTION PROGRESS UPDATE

Utility Work Completed to Date

Century Link

- Relocated facilities affecting over 5,000 homes
- Upgraded the Oak Hills Drive area internet speed
- Conduit for future fiber expansion was also installed

CONSTRUCTION PROGRESS UPDATE

Project to Date

Paving on the Eastside
Frontage Road, Nov 2020



CONSTRUCTION PROGRESS UPDATE

Project to Date

View looking south at the
future 200/400 North
interchange, Dec 2020



UPCOMING CONSTRUCTION ACTIVITIES

200 North/400 North

- Working in the area of the old northbound lanes through the winter
 - Milling
 - Excavating
 - Utility installation
- Bridge deck construction in early spring
- Green Road/Bair Creek
 - Pedestrian box through February
- West Frontage Road
 - Utilities and detention pond excavation

UPCOMING CONSTRUCTION ACTIVITIES

Gordon Avenue

- Utility work on the east side, while traffic flows on the southbound lanes
- Bridge work
 - Currently: support beams and foundation
 - Spring: bridge deck
- Cast-in-Place Wall Construction along East Side Drive from 1070 N to North Village Dr.
- Gordon Extension will resume in the spring



UPCOMING CONSTRUCTION ACTIVITIES

Oak Hills Drive


- Traffic switch to the southbound lanes December 18-21
 - Excavation and utility construction will begin
- Bridge construction
 - Walls
 - Abutments
 - Girders
 - Bridge deck in early spring
- West Frontage Road between 2800 East and Crestwood
- Excavation and utilities through the winter



UPCOMING CONSTRUCTION ACTIVITIES

Antelope Drive

- West side utilities through the winter
- Intermittent closures at Country Oaks Lane, 1975 N and Oak Lane for water, sewer & storm drain
- North of Antelope for CenturyLink, Comcast, water

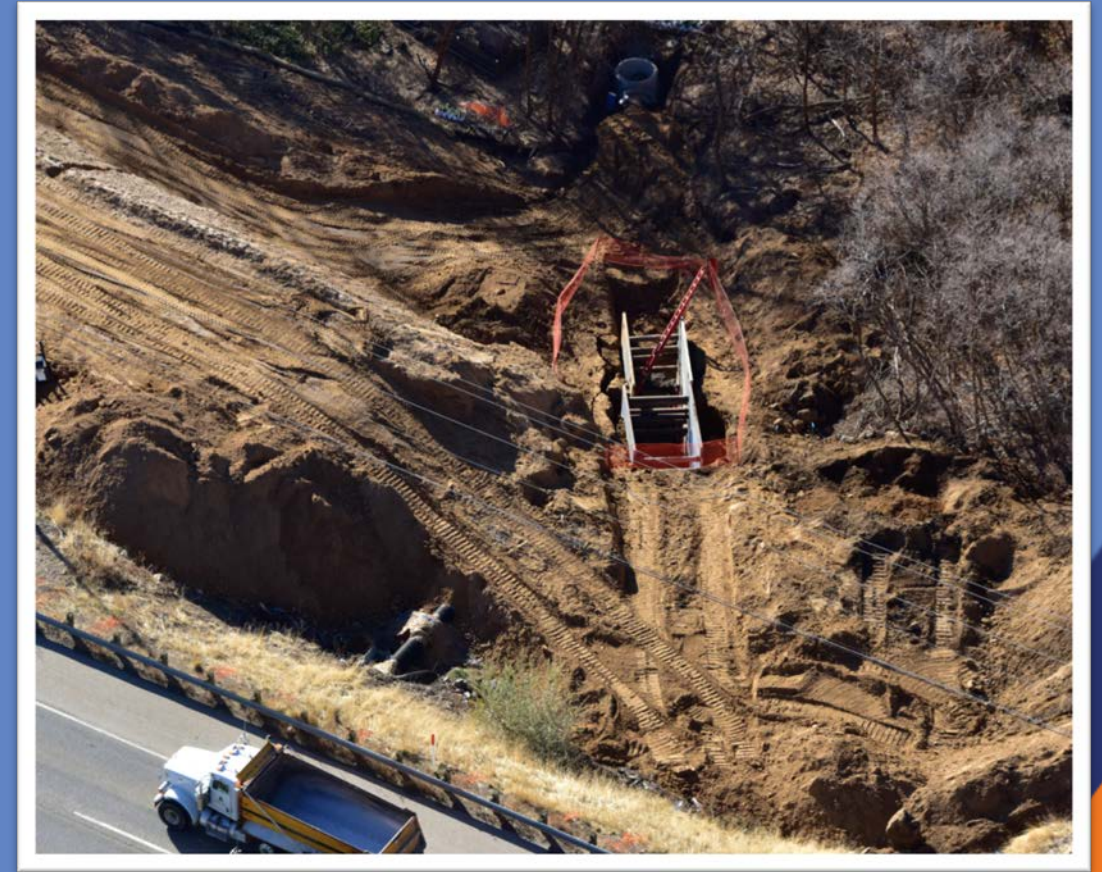

CCT MEMBER FEEDBACK

- Project questions?
- What are you hearing from neighbors?
- Any information needs?
- How can we help you keep people informed?
- Is there anything you think could improve the CCT process?

VOTING

Please consider your evaluation of Oak Hills Constructors
according to the agreed upon areas of evaluation from
October 21– December 17, 2020.

<https://publicinput.com/US89CCTDec2020>



OTHER QUESTIONS OR ITEMS FOR DISCUSSION?

NEXT CCT MEETING – February 18, 2020

U.S. 89 TEAM CONTACTS

Communications Team

- Aubry Bennion
- Leah Jaramillo

Email: us89@utah.gov

Web: udot.utah.gov/US89

Hotline: 888.752.8789

Facebook: [@US89DavisCounty](https://www.facebook.com/US89DavisCounty)
